Barlia Footbal Complex
Tender Programme

ID	Name
2	**Construction Period**
3	**Downtakings**
4	Remove Doors & Retain
5	Remove Benches & Lockers
6	Isolate Services
7	Isolate & Remove Fire Detection System & Retain
8	Remove Pipe Work & Cap
9	Remove Electrical FF&E
11	Remove Sanitary Ware
12	Remove Radiators
13	Remove Suspended Ceilings
10	Remove Reception Desk
14	Electrical Strip Out
15	Remove Vinyl Flooring & Skirtings
16	Remove Block Work Walls
17	Remove Floor Tiles to Changing Rooms/Shower Areas
19	Cut Floor For New Drainage Runs
18	Remove External Doors & Temp Infill
20	**Fit Out**
21	Electrical 1st Fix (Containment)
22	Block Work Walls
23	Below Ground Drainage
24	Plumbing 1st Fix (Drainage & Water Supplies)
25	Electrical 2nd Fix (Cabling)
26	Heating 1st Fix (New Pipe Runs)
27	Alterations to Existing Ventilations Services
28	Remedial Works to Floors
30	Wall Linings to Shower Areas
29	Decoration 1st Coat to Walls
31	Doors Sets, Finishing's & Ironmongery
32	Suspended Ceilings
35	Kitchen & Servery Installation
36	Electrical 3rd Fix (FF&E)
38	Decoration to Doors
33	Decoration 2nd Coat to Walls
37	Reinstate Fire Detection Heads
39	New Vinyl Flooring
40	Sanitary Wear
34	Heating 2nd Fix (Radiators)
41	Toilet & Shower Cubicles
43	Feature Suspended Ceiling
42	Lockers & Benches
44	Reception Desk
45	Power,Data,Alarms to Reception Areas

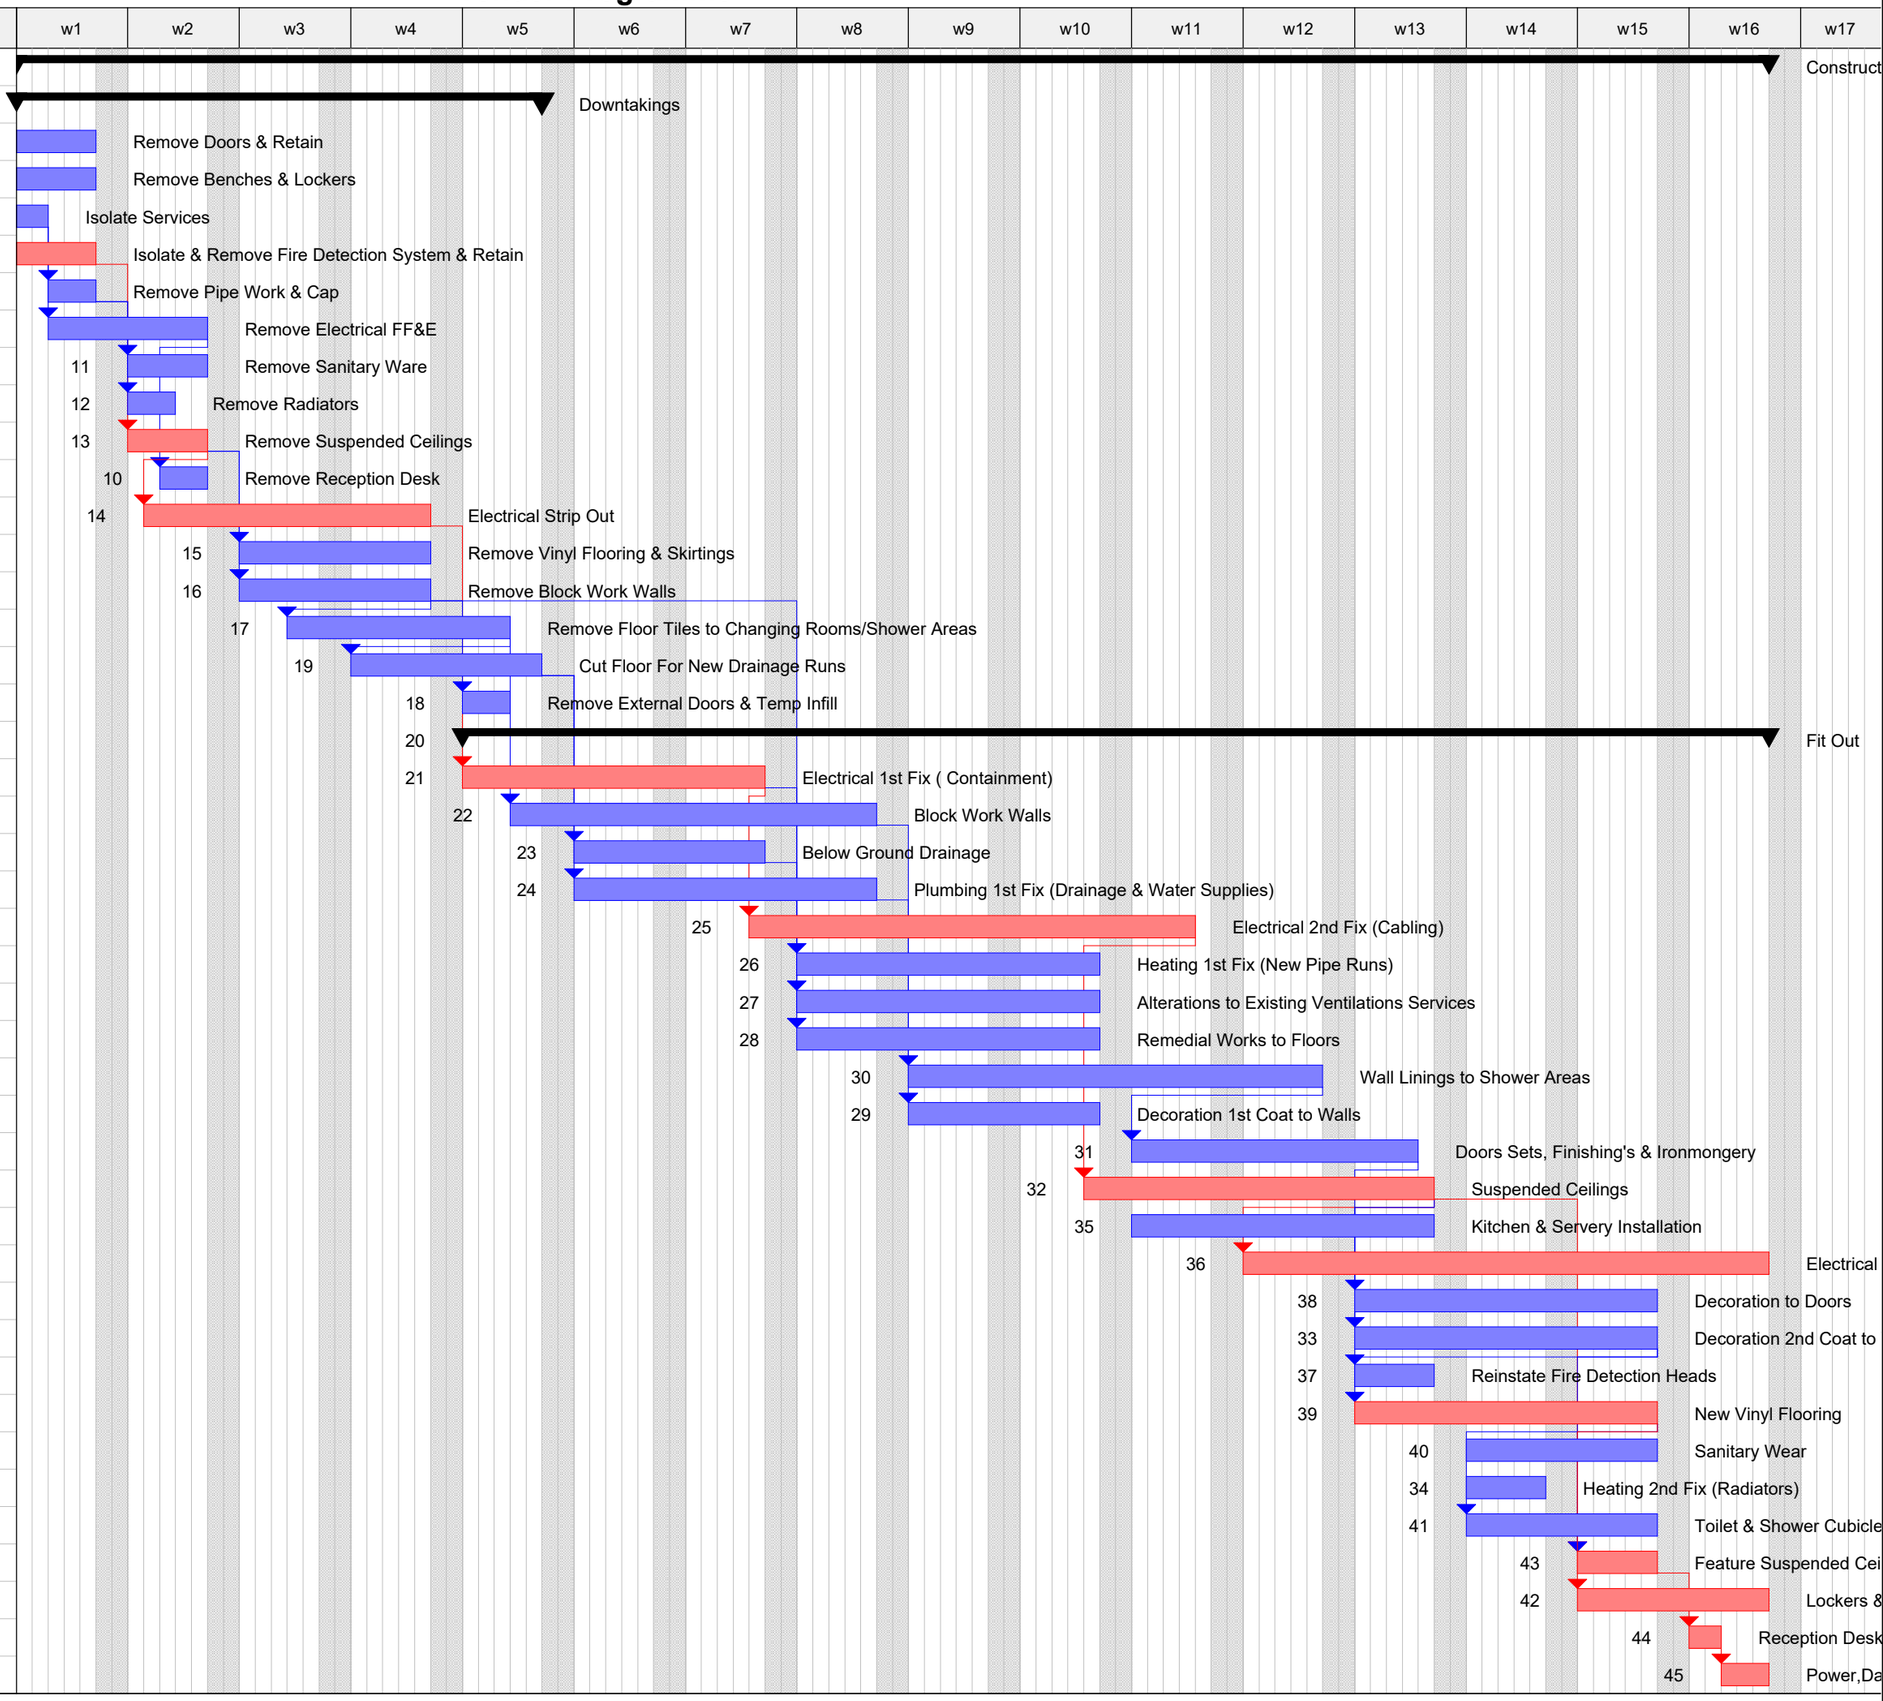

Detail Normal | Summary Normal | Detail Critical | Summary Critical | Detail Super-Critical | Summary Super-Critical | Baseline1 | Project | Percent Complete | Milestone | Baseline1 Milestone
